



Construction of the Science Building



MIDDLE TENNESSEE
STATE UNIVERSITY


Issue 11

4/11/2013

Gearing up for Spring

Turner
Building the Future

No winter lasts forever; no spring skips its turn.



Up to Date

- Area D Glazing 90% Complete
- Area A Concrete Complete
- Area D Exterior Masonry 90% Complete
- In slab rough in Area D lecture halls

In the Now

- Area A Roofing
- Area A Exterior Framing and sheathing
- Area D Duct Work Installation
- Area A Concrete Encased Columns
- Monumental Stairs in Atrium
- Metal Panel Install Area D Penthouse
- Area C Glazing and Curtain Wall Install

A Look Ahead

- Area B Slab on grade Pour
- HVAC Units Install Area D Penthouse 4/16-18
- Area C Masonry



Above: Lecture halls on the North side of area D are progressing with structural steel, concrete encased columns, and in slab rough-ins all complete. In the background area D curtain wall is nearly complete and workers are installing metal panels in the penthouse on the top floor.

The Breakdown

Man-hours	140,382
Concrete	7,920 cy
Decking	250,000 sf
Steel	1,750 tons

Right: Masonry wraps up in area D with workers cleaning the brick and removing plastic from the windows as they work their way back down the building.



Left: Ductwork makes its way through the 3rd floor and interior metal framing is also progressing. This view is down one of the main corridors in area D where individual rooms are being divided up and taking shape.

Today	Fri	Sat	Sun	Mon
Apr 11	Apr 12	Apr 13	Apr 14	Apr 15
Strong thunderstorms	Partly sunny	Mostly sunny	Mostly sunny and nice	A thunderstorm possible
73° Lo 44°	66° Lo 39°	67° Lo 41°	79° Lo 58°	76° Lo 65°








OxBlueTM

Construction Camera Service

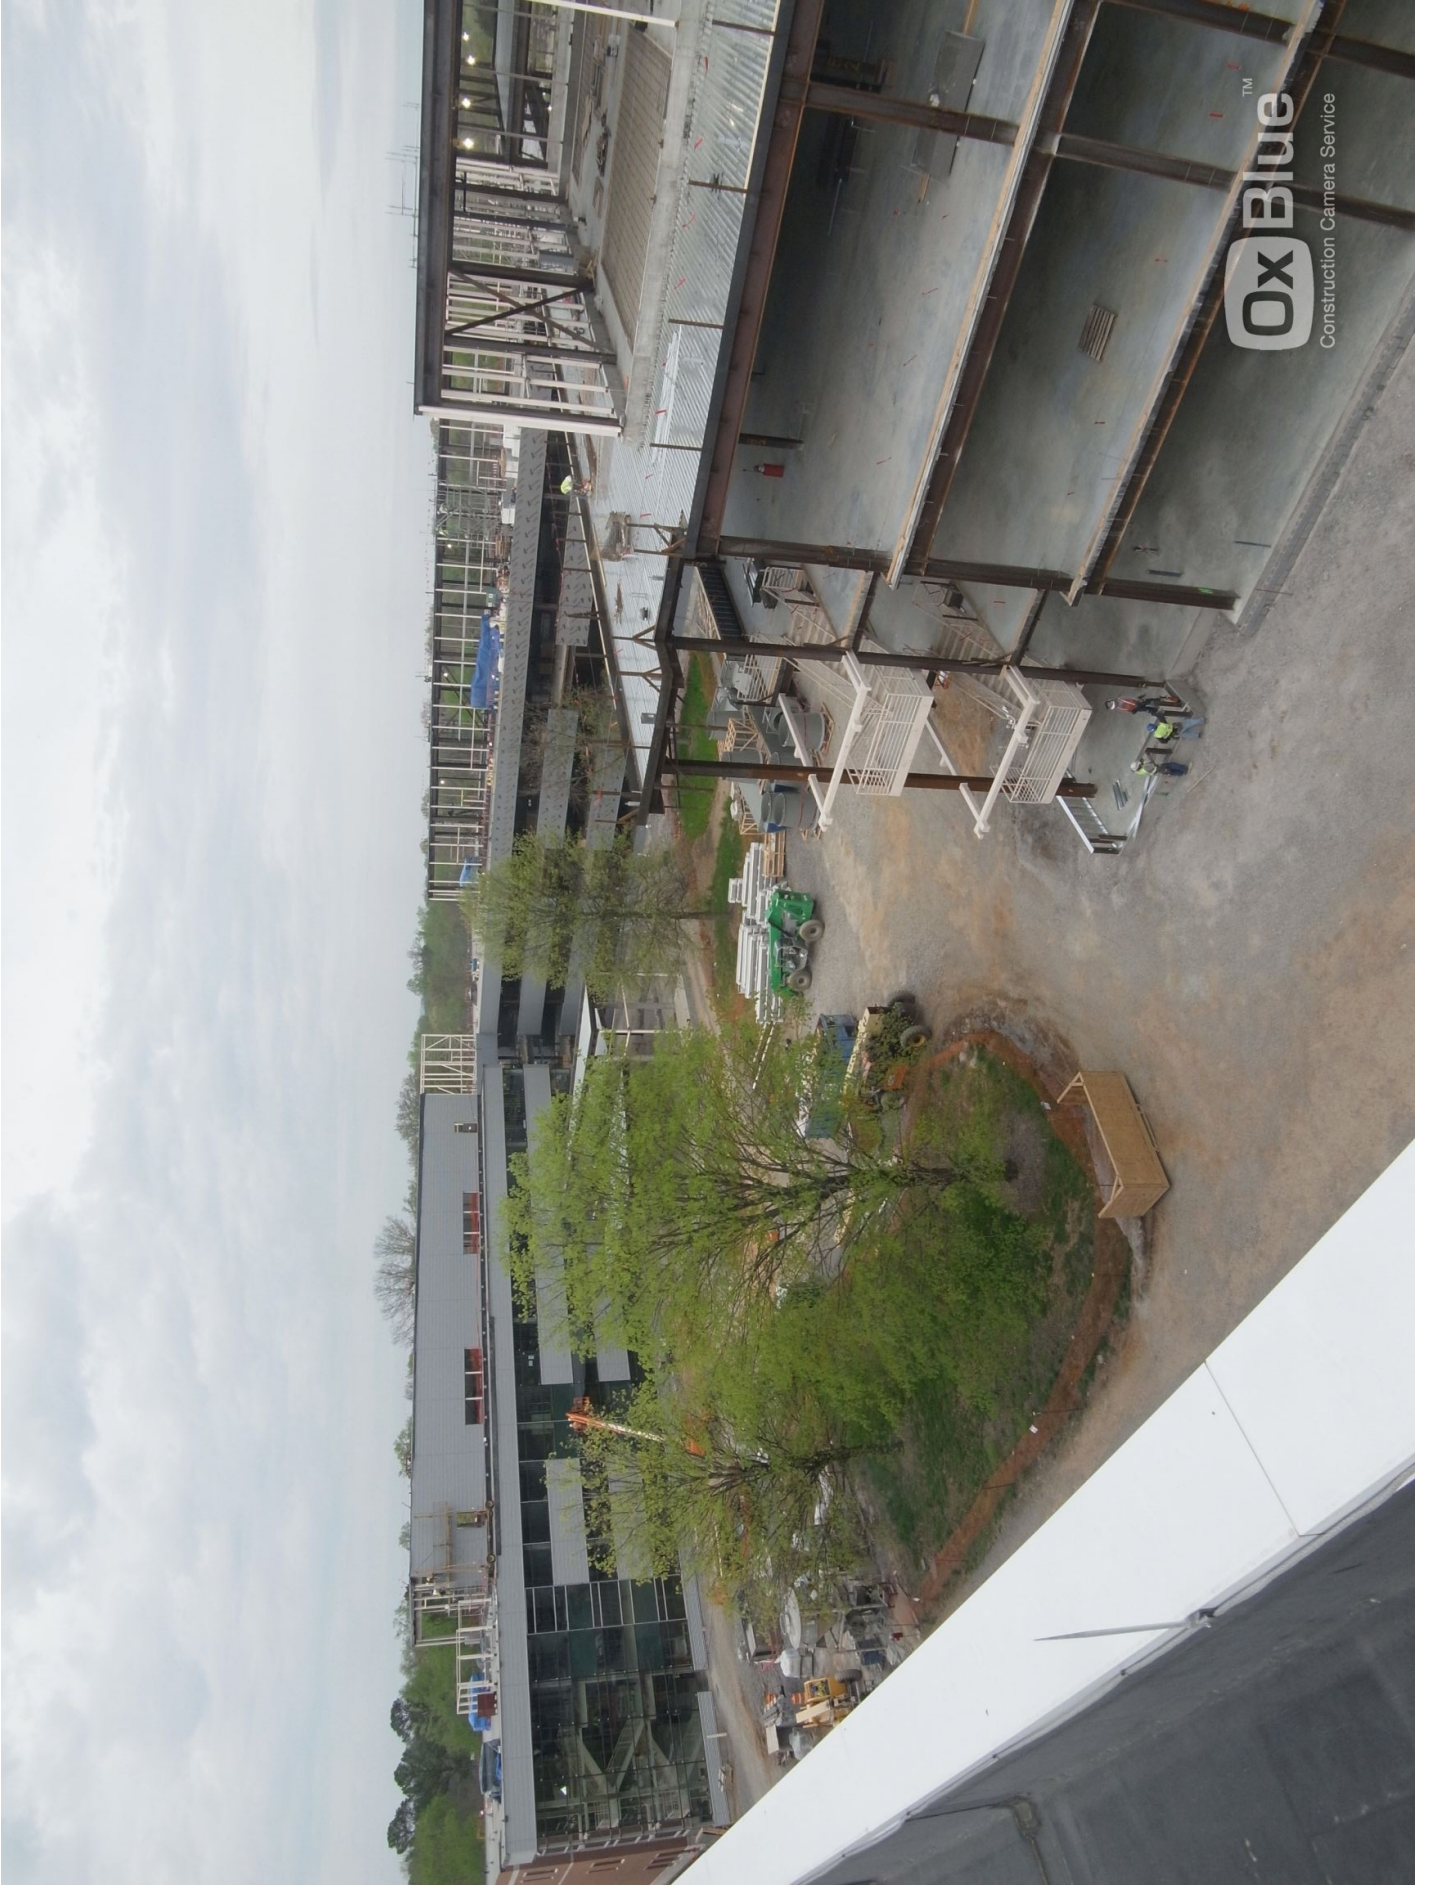

OxBlueTM

Construction Camera Service
